

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Disaster Relief Supply & Volunteer Coordinator (DRSVC)

Kishan S | PES2UG23CS277

Backlog Summary


Key	Type	Priority	Points
DRSVC-1	Epic 1: Supply Request & Dispatch Prioritization	High	8
DRSVC-2	Epic 2: Volunteer Matching & Roster Management	High	11
DRSVC-3	Epic 3: Delivery Tracking & Alerting	High	13
DRSVC-4	Story 1.1: Supply-Stock Matching	High	5
DRSVC-5	Story 1.2: Priority-Based Dispatch	High	3
DRSVC-6	Story 2.1: Nearest Volunteer Matching	High	8
DRSVC-7	Story 2.2: Volunteer Skill & Availability Registration	Medium	3
DRSVC-8	Story 3.1: Real-Time Delivery Dashboard	High	8
DRSVC-9	Story 3.2: Delivery Delay Alerts	Medium	5

Sprint Plan

Sprint 1 (Sep 10 – Sep 17, 2026): DRSVC-4, DRSVC-5, DRSVC-6, DRSVC-9 — 21 points. Goal: Enable the core supply-dispatch and volunteer-assignment workflow.


Sprint 2 (Sep 15 – Sep 17, 2026): DRSVC-7, DRSVC-8 — 11 points. Goal: Give disaster managers real-time operational visibility.

Sprint 1 Burndown Chart

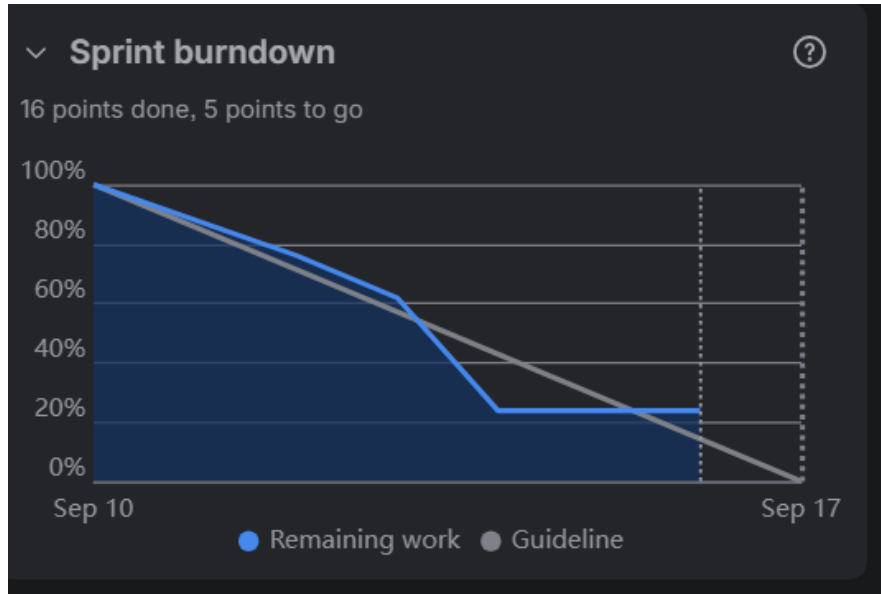


Sprint 1 burndown (Sep 10–17): 16 of 21 points completed at this snapshot; sprint closed with all 4 stories Done.

Sprint 2 Board & Burndown

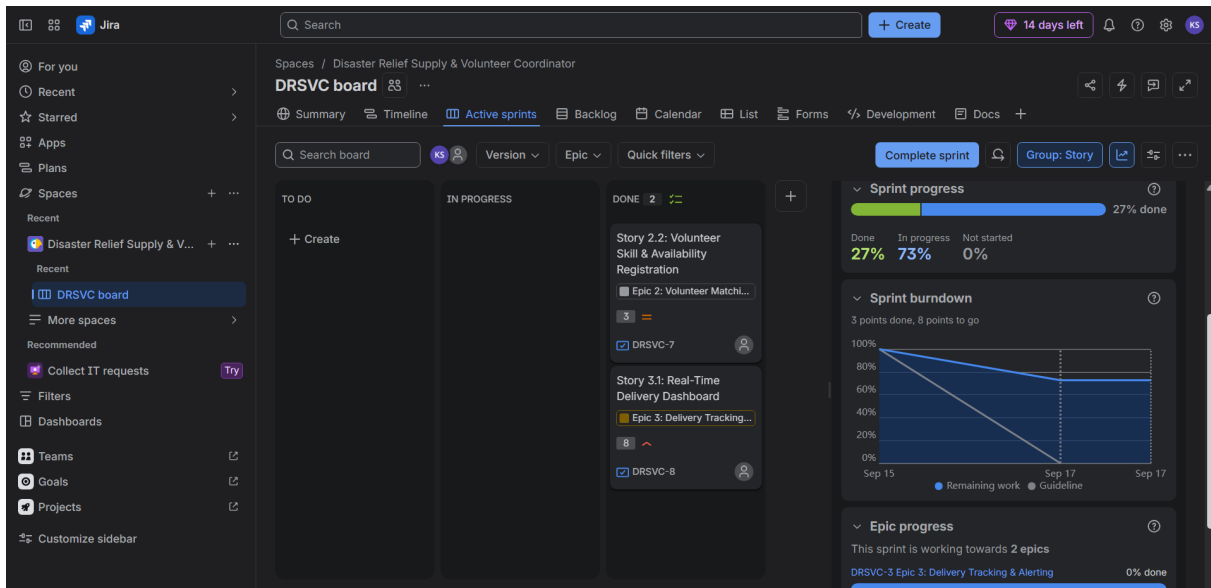

Sprint 2 Active Sprint board: both stories (DRSVC-7, DRSVC-8) moved to Done, with burndown panel visible on the right.

Sprint 2 Burndown Chart (detail)

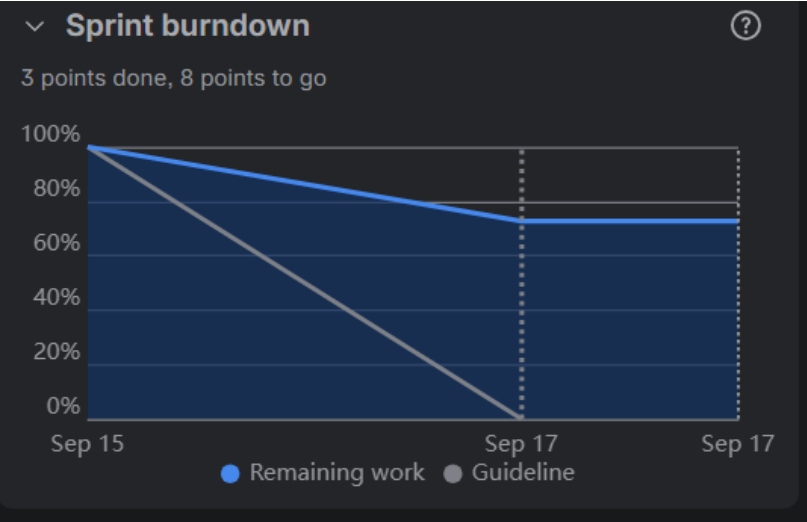

Sprint 2 burndown detail view.

Reflection Questions

1. Did your estimations reflect the actual effort?

The estimates were assigned using relative complexity rather than raw hours. Stories involving real-time components — Nearest Volunteer Matching (8 pts) and the Real-Time Delivery Dashboard (8 pts) — were sized higher because they depend on continuously changing external data (location, availability) and tighter response-time criteria. Simpler CRUD-style stories, like Volunteer Skill & Availability Registration (3 pts), were sized lower. Sprint 1's burndown shows a reasonably steady completion rate against the 21-point guideline, suggesting the estimates were broadly workable, though the flatter section mid-sprint indicates one story (likely the 8-point Nearest Volunteer Matching) took longer relative to its estimate than the smaller stories did.

2. Was your backlog well-prioritized?

Priority followed the original Functional Requirement priority levels from Lab 1: the three High-priority FRs map to the stories most critical to life-safety outcomes (supply matching, dispatch prioritization, volunteer matching, and the delivery dashboard), while the Medium-priority FRs (volunteer self-registration, delay alerts) were scheduled as supporting capabilities. Sequencing Sprint 1 around dispatch and volunteer assignment before Sprint 2's tracking/alerting layer also reflects a logical dependency order: you need a working assignment system before monitoring it.

3. How did your simulated sprint align with your plan?

Sprint 1 completed all 4 planned stories (21 points) within its window, and Sprint 2 completed both planned stories (11 points). Both sprints closed with 100% of their planned scope delivered, meaning no stories had to be pushed to a later sprint or descoped mid-sprint. This suggests the initial sprint planning correctly matched the team's simulated capacity to the work committed.

4. What insights did the burndown chart give about your team's capacity?

The Sprint 1 chart shows the remaining-work line tracking close to the guideline for the first part of the sprint before flattening briefly and then dropping to completion — a pattern consistent with one larger story (8 points) being worked on for an extended stretch before being marked Done, rather than steady incremental progress. Sprint 2's smaller, 11-point scope burned down faster and more predictably. Together, this suggests future sprints could benefit from breaking 8-point stories into smaller sub-tasks to produce a smoother, more predictable burndown.
